Board of State and Community Corrections (BSCC). In-Custody Death Review (ICDR) Division – Project Management Plan

Solicitation Number: RFO# ICDR0006

Technical Response Exhibit A – Scope of Work

Date of Submittal: Feb 10, 2026 5:00 PM PT

Submitted To:
procurement@bscc.ca.gov

Submitted By:
Kamaldeep Singh Arora
Vice President
554 Kilsyth CT, Folsom, California
Phone No.: (669)455-0349
Email: kamal.singh@radixsol.com

Table of Contents

1. Introduction & Understanding of the Engagement 1
2. Objectives….. 1
3. Executive Summary of Our Approach 1
4. Detailed Approach & Work Plan 2
5. Governance, Quality, and Reporting 5
6. Deliverables, Timing & Responsible Role (Mapped to Exhibit A) 5
7. Key Personnel & Role Responsibilities 7
   7.1. Resumes 8
8. Milestone Schedule (High-Level) 13
9. Acceptance Criteria & Reporting Compliance 13
10. Compliance Statement 14

1. Introduction & Understanding of the Engagement

The Board of State and Community Corrections (BSCC) has established the In-Custody Death Review (ICDR) Division pursuant to Senate Bill 519. The ICDR Division is responsible for reviewing investigations of deaths occurring in local detention facilities, issuing recommendations to local agencies, monitoring implementation, and providing information to the public. As a newly formed division, ICDR must simultaneously meet ongoing statutory oversight responsibilities while establishing the foundational governance, processes, and documentation required for long-term operational sustainability.

BSCC therefore seeks professional project management methodologies and coaching to support the development of structured governance, standardized processes, and supporting tools that enable compliant, transparent, and sustainable operations. The operating environment requires disciplined prioritization, formal governance, and coordinated execution to support the Division's transition from reactive operations to a mature and proactive oversight model.

Radixsol's engagement approach is designed to define and institutionalize Purpose, Mission, and Vision; translate strategy into a prioritized and resourced project portfolio; implement a tailored project management methodology; develop governance policies and SOPs; provide leadership coaching with measurable performance tracking; and deliver comprehensive knowledge transfer culminating in a complete Operational & Training Manual. All services will be performed during State business hours, with onsite support provided when requested and approved by BSCC; otherwise, services will be delivered virtually.

2. Objectives

Radixsol's objectives for this engagement are to support BSCC in fully establishing and sustaining the ICDR Division by:

- Defining and adopting clear Purpose, Mission, and Vision statements to guide internal operations and external communication
- Developing a Three-Year Strategic Goals Framework translated into measurable KPIs and milestones
- Establishing a prioritized project portfolio supported by signed project charters and resource-loaded schedules for three high-priority initiatives
- Developing and approving three governance policies and ten SOPs, maintained in a centralized repository with version control
- Implementing a tailored project management methodology compatible with BSCC's existing State-licensed tool environment and supported by training materials
- Providing leadership coaching with quarterly logs, confidential summaries, and performance metrics reviewed on a semi-annual basis
- Ensuring durable knowledge transfer through delivery of a Comprehensive Operational & Training Manual that supports operational independence

3. Executive Summary of Our Approach

Radixsol will deliver this engagement through five integrated phases—Discovery, Strategic Design, Operational Development, Leadership Coaching, and Knowledge Transfer—aligned with

Exhibit A timelines and acceptance criteria. The approach emphasizes single-point accountability, structured governance, and a project management methodology tailored to BSCC's operating environment.

All deliverables will be prepared in State-usable formats and submitted for formal State acceptance prior to invoicing, in accordance with Exhibit B payment provisions. The engagement is designed to support day-to-day statutory operations while building the long-term governance and operational infrastructure required under SB 519.

4. Detailed Approach & Work Plan

Radixsol will establish a formal project governance structure to support transparent decision-making, coordinated execution, and proactive risk management throughout the engagement. Governance will be anchored by a Project Steering Committee consisting of the ICDR Director, a designated BSCC representative, and the Radixsol Senior Project Management & Strategy Lead Fig 1. Steering reviews will address portfolio status, risks and issues, performance metrics, and decisions requiring leadership alignment.

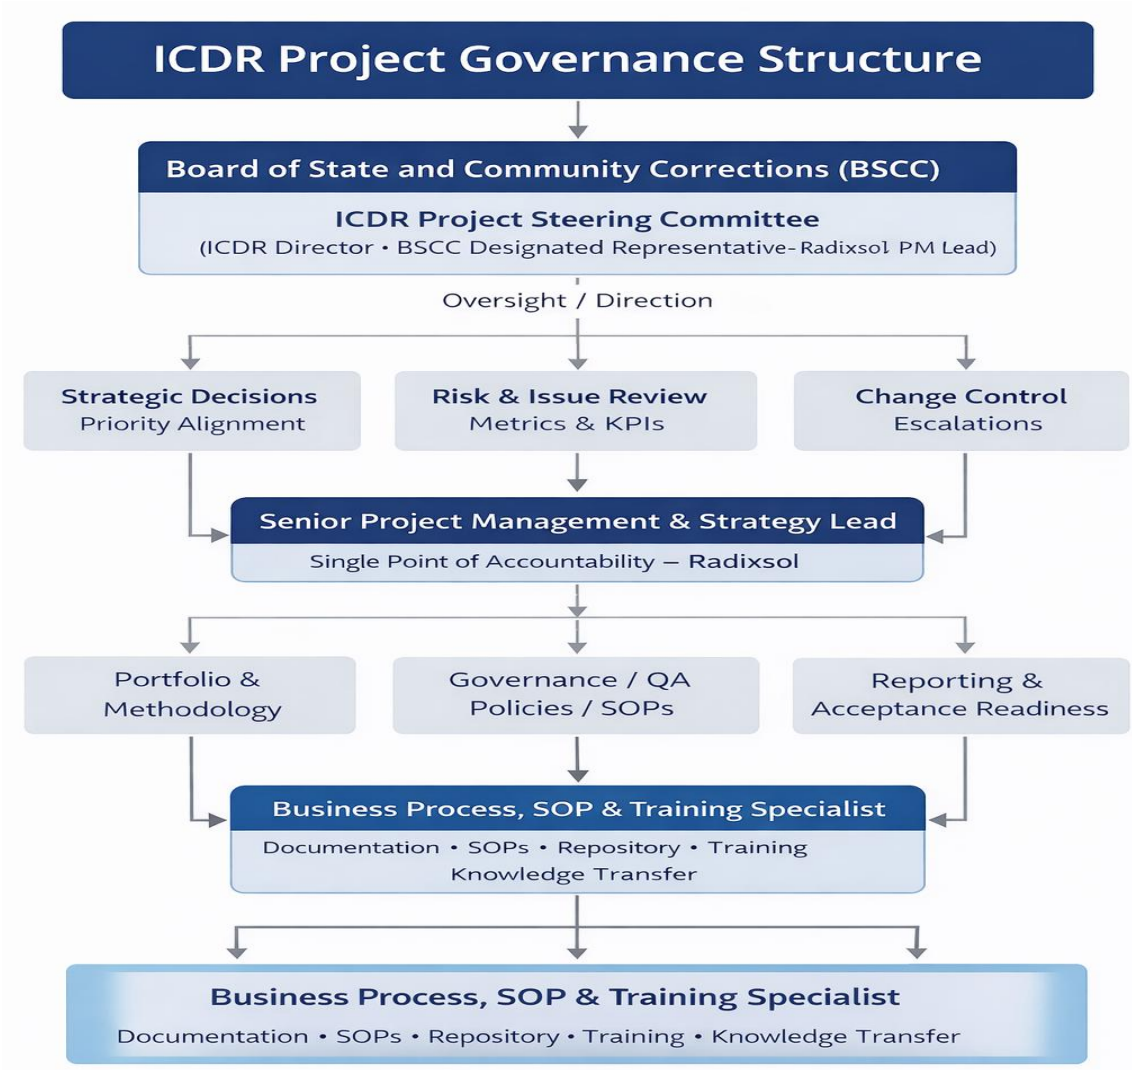

Fig 1: Project governance structure

Any baseline readiness activities conducted during Phase 1 are strictly diagnostic in nature and are intended solely to inform subsequent work products; the formal Project Management Maturity Assessment required under Exhibit A will be delivered at Month 12 in full compliance with State requirements.

To reinforce control and accountability, Radixsol will implement a formal change control process, defined escalation paths, and a maintained Risk and Issue Log documenting probability, impact, mitigation strategy, assigned owner, and review cadence.

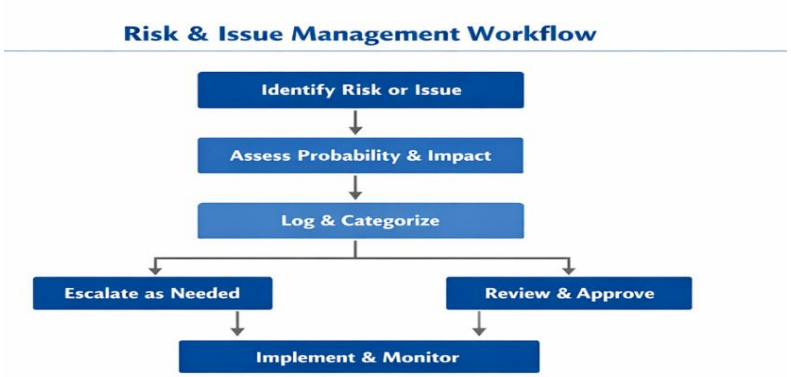

The delivery model combines single-point accountability with dedicated delivery support. The Senior Project Management & Strategy Lead serves as the sole point of accountability for deliverables, acceptance readiness, and schedule performance. A Business Process, SOP & Training Specialist supports documentation, SOP development, repository configuration, and training delivery under the Lead's direction. The engagement is structured into phased workstreams progressing from assessment and alignment through design, implementation, optimization, and sustainability. (Fig 2)

Fig 2: Five Integrated Phases

Phase 1 — Discovery, Readiness & Alignment (Months 1–3)

Purpose: Establish baseline readiness and align leadership on direction and governance.

Activities

- Conduct stakeholder interviews and review existing workflows, documentation, and operational artifacts
- Perform a Baseline Project Management Readiness Scan to identify current practices, gaps, and improvement opportunities
- Facilitate collaborative workshops to define Purpose, Mission, and Vision and document outcomes

Deliverables

- Session Summary Report (5–10 pages) with minutes and attendance (end of Month 3)
- One-page draft Purpose, Mission, and Vision statements
- Baseline Readiness Scan summary to inform subsequent phases

Note: The formal Project Management Maturity Assessment required by Exhibit A, including industry-standard scoring and five prioritized recommendations, will be delivered at Month 12.

Phase 2 — Strategy & Methodology (Months 4–9)

- Finalize Purpose, Mission, and Vision and publish the Mission on the public website and in two public-facing documents
- Develop Three-Year Strategic Goals consisting of 3–5 goals, each with defined KPIs and milestones
- Design a tailored project management methodology incorporating lifecycle stages, stage gates, governance checkpoints, and standard artifacts
- Develop three formally approved, version-controlled governance policies incorporating the approved Purpose and Vision and including a mandated annual review cycle
- Produce a Tool Recommendation Report aligned with existing State-licensed software subscriptions and required features
- Establish a centralized SOP repository with defined access controls and version management

Phase 3 — Operational Development & Portfolio Implementation (Months 10–15)

- Identify and prioritize three high-priority infrastructure initiatives
- Develop a Comprehensive Infrastructure Maturity Project Plan supported by signed project charters and detailed, resource-loaded schedules
- Develop ten approved SOPs delivered in three structured waves (3, 4, 3)

- Deliver staff training on methodology, SOPs, and tools supported by quick-reference guides

Phase 4 — Leadership Coaching & Performance Optimization (Months 1–18)

- Provide quarterly one-on-one leadership coaching for each leadership team member with documented logs and confidential summaries
- Establish and monitor three leadership performance metrics reviewed every six months

- Illustrative leadership performance metrics may include targets such as: 90% of active initiatives supported by approved project charters; a 20% reduction in recurring meeting time through agenda discipline and decision logs; and on-time completion of 85% or more planned milestones, with final metrics established collaboratively with ICDR leadership.

Phase 5 — Knowledge Transfer & Sustainability (Months 16–18)

- Deliver a Comprehensive Operational & Training Manual including how-to guides, process flow diagrams, and troubleshooting FAQs
- Conduct structured handoff sessions and a final sustainability assessment

5. Governance, Quality, and Reporting

- Monthly steering reviews with defined escalation paths
- Central Risk and Issue Log with probability, impact, mitigation, ownership, and review cadence
- Risk and Issue Logs will be reviewed at each Steering Committee meeting
- Formal change control process
- Internal QA review for each deliverable prior to submission
- Monthly timesheets and status reports, with ad-hoc reporting as requested
- Deliverables submitted for formal State acceptance prior to invoicing
- Invoices submitted monthly in arrears with ten percent (10%) retention until final completion
- Work performed 8:00 a.m.–5:00 p.m. PST unless pre-approved; travel reimbursed in accordance with CalHR rates

6. Deliverables, Timing & Responsible Role (Mapped to Exhibit A)

The table below maps each Exhibit A required task and performance measure to Radixsol's corresponding deliverables, delivery timing, and responsible role. All deliverables will be submitted in State-usable formats and are subject to formal State acceptance prior to invoicing.

Exhibit A Requirement / Performance Measure	Radixsol Deliverable	Target Timing	Responsible Role
Facilitate collaborative sessions to define Purpose, Mission, and Vision	Three facilitated workshops with ICDR leadership and staff	Months 1–3	Senior Project Management & Strategy Lead
Produce Session Summary Report including minutes and attendance	Session Summary Report (5–10 pages) documenting minutes, attendance, themes, and action items	End of Month 3	Senior Project Management & Strategy Lead
Produce one-page draft Purpose, Mission, and Vision	Draft Purpose, Mission, and Vision document for leadership review	Month 3	Senior Project Management & Strategy Lead

Provide finalized and approved Purpose, Mission, and Vision	Final signed Purpose, Mission, and Vision statements ready for publication	Month 6	Senior Project Management & Strategy Lead
Publish Mission on public website and in public-facing documents	Website-ready Mission statement and integration into two public-facing documents	Month 6	Senior Project Management & Strategy Lead
Develop three (3) internal governance policies	Draft governance, change management, and operational alignment policies	Month 6	Senior Project Management & Strategy Lead
Finalize and approve three (3) internal governance policies	Final, approved, version-controlled policies incorporating Purpose/Vision and including a mandated review cycle	Month 12	Senior Project Management & Strategy Lead
Facilitate Three-Year Strategic Goals setting	Strategic goal-setting workshops with ICDR leadership	Months 4–6	Senior Project Management & Strategy Lead
Provide Three-Year Strategic Goals with KPIs and milestones	Three-Year Strategic Goals Framework with KPIs and milestones	Month 6	Senior Project Management & Strategy Lead
Establish SOP repository structure	Centralized SOP repository with access controls, version tracking, and naming conventions	Month 4	Business Process, SOP & Training Specialist
Develop Standard Operating Procedures (SOPs)	SOP Wave 1 – Three (3) approved SOPs	Month 8	Business Process, SOP & Training Specialist
Develop Standard Operating Procedures (SOPs)	SOP Wave 2 – Four (4) approved SOPs	Month 10	Business Process, SOP & Training Specialist
Develop Standard Operating Procedures (SOPs)	SOP Wave 3 – Three (3) approved SOPs	Month 12	Business Process, SOP & Training Specialist
Design tailored Project Management Methodology	Draft Project Management Methodology incorporating lifecycle stages, stage gates, and governance checkpoints	Month 6	Senior Project Management & Strategy Lead
Finalize tailored Project Management Methodology	Final Project Management Methodology Framework	Month 8	Senior Project Management & Strategy Lead
Produce Tool Recommendation Report	Tool Recommendation Report aligned with existing State-licensed software subscriptions and required features	Month 8	Senior Project Management & Strategy Lead

Identify high-priority infrastructure projects	Infrastructure project identification and prioritization documentation	Month 10	Senior Project Management & Strategy Lead
Provide comprehensive infrastructure project plan	Comprehensive Infrastructure Maturity Project Plan	Month 10	Senior Project Management & Strategy Lead
Produce signed project charters	Three formally signed Project Charters	Month 12	Senior Project Management & Strategy Lead
Provide detailed, resource-loaded project schedules	Three resource-loaded schedules with dependencies and milestones	Month 12	Senior Project Management & Strategy Lead
Perform Project Management Maturity Assessment	Formal PM Maturity Assessment Report with scoring, gap analysis, and five prioritized recommendations	Month 12	Senior Project Management & Strategy Lead
Provide leadership coaching	Quarterly one-on-one leadership coaching sessions and logs for each leadership team member	Quarterly (Months 1–18)	Senior Project Management & Strategy Lead
Provide confidential leadership summaries	Confidential quarterly leadership summaries	Quarterly (Months 1–18)	Senior Project Management & Strategy Lead
Monitor and report performance metrics	Semi-annual performance metric review documentation	Every 6 months	Senior Project Management & Strategy Lead
Develop training materials and job aids	Training decks and quick-reference guides	Months 10–12	Business Process, SOP & Training Specialist
Provide knowledge transfer documentation	Comprehensive Operational & Training Manual (how-to guides, process flows, troubleshooting FAQs)	Closeout	Business Process, SOP & Training Specialist
Conduct formal handover	Final transition and handover package	Closeout	Senior Project Management & Strategy Lead

7. Key Personnel & Role Responsibilities

- Senior Project Management & Strategy Lead — Engagement Lead and Single Point of Accountability
- Business Process, SOP & Training Specialist — Documentation, SOP development, training, and manual preparation
- The Senior Project Management & Strategy Lead will provide approximately 60–70% level of effort across the engagement, with peak support from the SOP Specialist during documentation and training phases. Senior Project Management & Strategy Lead availability will be adjusted as needed to address emergent statutory, operational, or risk-

driven priorities identified by BSCC, ensuring continuous leadership support throughout the engagement.

Staffing levels will be scaled to align with each phase of work, with the Senior Project Management & Strategy Lead providing primary oversight and delivery accountability throughout the engagement, and the Business Process, SOP & Training Specialist providing focused support during documentation, SOP development, training, and knowledge transfer-intensive phases. Resource allocation will be adjusted as needed to ensure timely delivery of all Exhibit A deliverables.

7.1. Resumes

Resume- Senior Project Management & Strategy Lead

Deepak Adlakha
Linked In ID **https://www.linkedin.com/in/deepinfo?utm_source=share_via&utm_content=profile&utm_medium=member_android**
Brief Summary
Senior Project Management & Strategy Lead with over 20 years of experience supporting public-sector organizations, including State of California agencies, county governments, and public safety departments. PMP-, CSM-, and ITIL-certified professional with demonstrated expertise in governance framework development, project portfolio management, policy and SOP authoring, organizational maturity assessments, and leadership coaching. Experienced in working within highly regulated environments involving public safety, healthcare, and sensitive data, with a strong record of translating statutory and executive directives into structured, compliant, and sustainable operational practices.
Education / Certification / Training/Awards
Masters in Computer Applications, Indira Gandhi National Open University Bachelors in Commerce, DAV College Faridabad **Project Management Professional (PMP)** – PMI (ID: 3529295) **Certified ScrumMaster (CSM)** – Scrum Alliance (ID: 1822178) **ITIL Foundation Certification** – (ID: 13553-771515)
Professional Experience
Strategic Program Lead & Governance Architect , Fire Department – City of Oklahoma **Apr 2023 – Present** **Responsibilities:** o Serve as a strategic advisor to Fire Department leadership, supporting governance, portfolio prioritization, and performance management initiatives. o Facilitate executive workshops to translate organizational goals into operational KPIs and actionable work plans. o Design and implement fiscal governance and budget oversight models, including budget-versus-actual tracking. o Support audit readiness through implementation of compliant financial and operational tracking mechanisms. o Improve workforce planning and operational readiness through resource allocation and staffing compliance initiatives.

- Develop and maintain training and certification tracking systems to ensure staff qualification compliance.
- Standardize monitoring of daily safety checks and operational SOPs.
- Support inter-agency coordination with police and medical integrated health (MIH) teams.

Police & Fire Departments, Senior Project Manager & Change Management Lead **Jan 2017 – Mar 2023**

Responsibilities:

- Managed governance and oversight initiatives for public safety and law enforcement operational workflows.
- Established standardized processes and SOPs for Computer Aided Dispatch (CAD) and Records Management Systems (RMS).
- Supported compliance requirements for handling sensitive public safety and law enforcement data.
- Led organizational change management activities, including training, stakeholder engagement, and adoption support.
- Facilitated steering committee meetings with Police and Fire Chiefs, IT leadership, and executive stakeholders.
- Implemented structured reporting mechanisms to support data integrity and operational transparency.

Senior Governance Lead & Business Process Architect, County of Solano, California – Department of Information Technology **Mar 2022 – Jun 2022**

Responsibilities:

- Designed and implemented a countywide data governance framework defining roles, responsibilities, and decision-making authority.
- Authored governance policies and SOPs related to data classification, access control, and PII/PHI handling.
- Conducted discovery and alignment workshops with department leadership to document current-state workflows and gaps.
- Integrated State and federal compliance requirements into governance and risk management plans.
- Developed operational documentation and delivered train-the-trainer sessions to support sustainability.

Project Manager & Process Analyst, California Department of Public Health (CDPH) **Feb 2018 – Jan 2021**

Responsibilities:

- Managed projects under State of California SIMM/SAM standards and Department of Finance reporting requirements.
- Analyzed and re-engineered vendor invoicing and approval workflows to improve processing efficiency.
- Developed standardized SOPs to support audit readiness and consistent execution.
- Designed executive dashboards to provide leadership visibility into budgets, timelines, and operational performance.
- Delivered training and job aids to support adoption of new reporting tools and processes.

Project Manager & Governance Lead, Southern California Association of Governments (SCAG) **Jul 2021 – Mar 2022**

Responsibilities:

- Led a fixed-bid enterprise project for a large public-sector organization involving multiple stakeholders.
- Managed cross-functional project teams and facilitated executive and procurement stakeholder alignment.
- Documented and standardized SOPs and governance artifacts supporting financial and reporting systems.
- Delivered knowledge transfer through structured train-the-trainer programs to ensure internal sustainability.

Senior Project Manager & Compliance Lead, Airrosti Rehab Center

Apr 2021 – Dec 2022

Responsibilities:

- Led governance and compliance initiatives for a multi-location healthcare organization.
- Ensured adherence to HIPAA requirements for handling sensitive patient information.
- Developed risk management and compliance tracking frameworks.
- Standardized reporting, QA processes, and operational documentation.
- Coordinated executives, SMEs, and vendors to maintain transparency and compliance.

Supporting Projects (Selected) **Jan 2003 – Feb 2018**

AG-Vendor, Technical Lead

Financial Systems Integration: Led the integration of QuickBooks and invoicing modules to streamline vendor payment workflows

BRMS, Process Architect

Organizational Assessment: Conducted a comprehensive "People, Process, Technology" assessment to identify operational gaps.

AG-MIS, BI Architect

Executive Reporting: Designed Sales Revenue Analysis dashboards to support C-level strategic decision-making.

ANCORF, Product Manager

Application Modernization: Managed the lifecycle of a low-code/no-code platform to accelerate internal development.

PABCO, Project Manager

Legacy Migration: Managed the risk and execution of migrating critical windows-based legacy applications to web platforms.

AMGEN , Change Lead

Collaboration Rollout: Managed the enterprise-wide rollout of MS Teams and SharePoint Online (SPO) for enhanced collaboration.

Dell-Quest, Project Manager

Service Management: Oversaw the implementation of a Request Queue Management product to optimize IT service delivery.

VSP, Project Manager

Digital Transformation: Managed the development of responsive digital interfaces for major insurance partner integration.

RevCore, Compliance Lead

Regulatory Transition: Managed the ICD9 to ICD10 transformation project, ensuring full compliance with medical coding standards.

RCM-PrognoCIS , Solution Architect

Operational Integration: Integrated multiple Revenue Cycle Management (RCM) products to unify daily operational workflows.

ALPS, Program Manager

M&A Technology Integration: Led the technology transformation and consolidation efforts during a major Banking/Insurance acquisition.

Resume- SOP Specialist

Dirk Buesing
Linked In ID **www.linkedin.com/in/dirk-buesing-mba-1118784**
Brief Summary
Senior Business Process and SOP Specialist with over 20 years of experience supporting California county government operations, including justice and probation environments. Extensive background in business process analysis, SOP development, user acceptance testing, training development, document control, and compliance-driven system implementations. Highly experienced in translating laws, regulations, and policy requirements into standardized procedures, workflows, and system configurations. Proven ability to support large-scale public-sector system implementations, ensure audit readiness, and deliver sustainable documentation and training for operational staff.
Education / Certification / Training/Awards
Master of Business Administration (MBA), Information Systems Management Diploma Finanzwirt (FH) / Bachelor of Science in Public Administration Fachhochschule für Verwaltung und Rechtspflege, Rinteln, Germany **Certificate in Purchasing Management**
Professional Experience
Business Process Analyst III, County of Riverside – Probation Department (via Radixsol) **Sept 2022 – Present** **Responsibilities:** o Serve as project lead for the Tyler Enterprise Supervision system implementation supporting probation operations. o Conduct complex business process and system analysis, including evaluation of current and proposed workflows and cost–benefit assessments. o Develop and document user requirements for new and existing systems, processes, and applications. o Prepare and maintain project documentation, requirements, feasibility studies, reports, and quality assurance artifacts. o Select and recommend software solutions based on system analysis and vendor evaluations; develop RFPs and technical specifications. o Design, implement, and maintain complex system configuration tables to ensure compliance with State and federal requirements. o Interpret and analyze new or revised regulations to identify required system and process changes. o Coordinate with departmental staff to implement system and process updates supporting new or modified public programs. o Conduct system testing and user acceptance testing prior to production release to ensure expected results.

- Provide SOP documentation, training, and functional guidance to staff supporting integrated enterprise systems.
- Coordinate system security and support network security and installation requirements.
- Supervise and train staff supporting business process and system improvement initiatives.

Senior Procurement Contract Specialist, County of Riverside, California
Mar 2019 – Sept 2022

Responsibilities:

- Provided technical supervision, training, and guidance to procurement and buyer staff.
- Developed and managed complex contracts for commodities and services across multiple County departments.
- Led competitive procurement processes including RFPs, RFQs, and Invitations to Bid.
- Drafted contract terms and conditions to protect County interests while ensuring vendor performance.
- Led negotiations involving end users, legal counsel, and technical experts.
- Reviewed procurement activities for compliance with County policies, codes, and cost-effectiveness standards.
- Developed and delivered training for County staff and external stakeholders on procurement policies and procedures.

Business Process Analyst II, County of Riverside, California **Jul 2008 – Mar 2019**

Responsibilities:

- Supported countywide implementation of Jaggaer (Source-to-Pay) integrated with Oracle/PeopleSoft Financials.
- Led design and evaluation of business processes supporting enterprise systems and upgrades.
- Developed and facilitated training for Jaggaer modules including Supplier Management, Contract Management, Sourcing, eProcurement, and Accounts Payable.
- Designed and maintained approval workflows for vendor registration, contracts, requisitions, and accounts payable.
- Conducted system testing and validation for Oracle/PeopleSoft and Jaggaer upgrades.
- Evaluated existing business processes to identify opportunities for automation and standardization.
- Served as subject-matter expert for procurement, contract management, accounts payable, and vendor registration systems.
- Developed Oracle/PeopleSoft queries and analyzed complex financial data to support executive reporting and audits.
- Supported countywide procurement and spend analysis initiatives, providing executive-level reporting and analysis.

Business Process Analyst I / Buyer II, County of Riverside, California
Mar 2006 – Jul 2008 / Dec 2003 – Mar 2006

Responsibilities:

- Supported procurement operations including commodity purchasing, vendor management, and contract administration.
- Prepared and evaluated complex bids and RFPs in support of County purchasing needs.
- Conducted market research, cost analysis, and life-cycle cost evaluations.
- Maintained vendor databases and procurement records.

- Developed Oracle/PeopleSoft queries and reports supporting purchasing and financial oversight.
- Provided functional support for Oracle/PeopleSoft Purchasing Module and participated in system testing activities.

Buyer I / Buyer Trainee / Accounting Assistant II, County of Riverside, California
Jun 2002 – Dec 2003 / Feb 2002 – Jun 2002

Responsibilities:

- Supported County purchasing, accounting, and procurement operations.
- Assisted with contract review, financial data collection, and system troubleshooting.
- Provided Oracle/PeopleSoft Financials support and training coordination.
- Supported Countywide financial and procurement reporting activities.

Diploma Finanzwirt (FH), Finanzamt Lüneburg (Germany)
Sep 1998 – Feb 2000

Responsibilities:

- Evaluated and processed individual and small business tax filings.
- Conducted internal audits of business financial records.
- Reviewed and processed tax appeals in accordance with applicable laws and procedures.
- Prepared written appeal decisions supporting formal finance court proceedings.

8. Milestone Schedule (High-Level)

- Month 3: Discovery complete; Session Summary Report; Draft P/M/V
- Month 4: SOP repository established
- Month 6: Final P/M/V; policies; PM methodology; Strategic Goals Framework
- Month 8: SOP Wave 1; Tool Recommendation Report
- Month 10: SOP Wave 2; Infrastructure Maturity Project Plan
- Month 12: SOP Wave 3; charters and schedules; PM Maturity Assessment
- Months 1–18: Coaching logs and metric reviews
- Closeout: Operational & Training Manual and final transition

9. Acceptance Criteria & Reporting Compliance

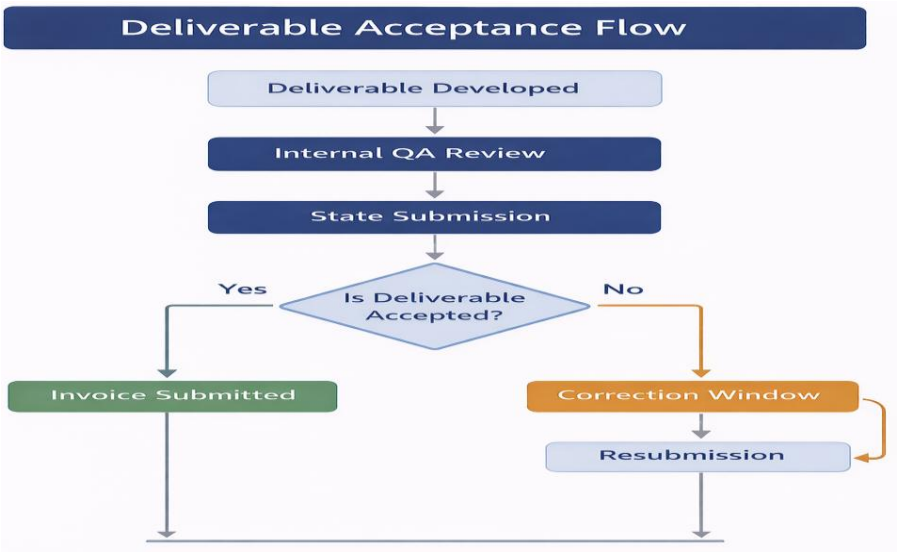

Fig 3: Deliverable Acceptance Flow

This flow illustrates Radixsol's internal quality review, State submission, acceptance, correction, and invoicing process in alignment with Exhibit A and Exhibit B requirements.

- Each deliverable is subject to **formal State acceptance** prior to invoicing.
- If a deliverable is not accepted, the State will provide written rationale in accordance with Exhibit A, and Radixsol will address the feedback and resubmit the deliverable within an agreed correction window to support timely acceptance and invoicing.
- **Monthly timesheets and status reports** will be submitted in State-usable formats to support oversight and acceptance.
- **Invoicing will be performed in accordance with Exhibit B** Budget Detail and Payment Provisions.

10. Compliance Statement

This Technical Response fully satisfies Exhibit A – Scope of Work and aligns with all mandated deliverables, timelines, acceptance criteria, reporting obligations, service hours, and standard terms and conditions referenced in the RFO package.
